
Final deliverable A. Three-month roadmap

Project: Fittybird x Kiabi, 360° Framework
Deliverable: A, Period 4 (sketch the path to project initiation)
Terms: `shared/glossary.docx`

The roadmap covers 12 working weeks, from Mon 2026-11-09 to Fri 2027-02-12, with a two-week holiday break. It is web first (sprints 1 to 3), then the store pilot (sprints 4 to 6), as decided in `00-bootstrap/03-growth-levers-and-web-first.docx`. Beyond three months there are too many unknowns, so nothing is planned past 2027-02-12.

The riskiest and most valuable items come first: privacy basics, the build-or-buy question and the avatar prototype are in the first four weeks.

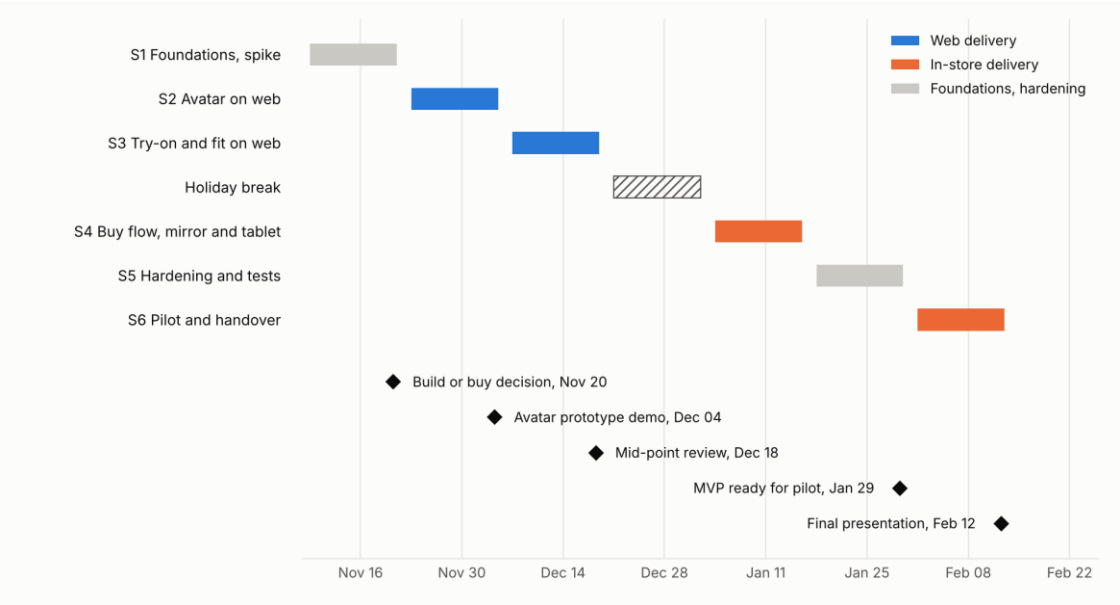

1. Sprint goals and victories

Sprint	Dates	Focus	Goal	Stories	Victory to celebrate
1	Nov 9 to Nov 20	Web	Prove the riskiest parts: privacy basics, sign-in, the avatar and try-on approaches, Kiabi data, and the platform they run on	SP-01, SP-02, OPS-01, PRIV-01, TECH-01, TECH-03, US-01, US-02, US-03	Build-or-buy decision made. Try-on approach chosen. First avatar from a test photo set. Four environments running
2	Nov 23 to Dec 4	Web	A working avatar in the app, with tracking	US-04, US-05, US-06, US-22, TECH-02	Each team member creates their own avatar end to end
3	Dec 7 to Dec 18	Web	Try-on and fit	US-07, US-08, US-09, US-10	A garment on a real avatar with its fit view, shown at the mid-point review
Break	Dec 21 to Jan 1	None	Rest	None	None
4	Jan 4 to Jan 15	Web and store	Buy flow and the in-store mirror and tablet	US-11, US-12, US-13, US-14, US-23, OPS-02	A size requested on the mirror appears on the staff tablet
5	Jan 18 to Jan 29	Web and store	Feedback, dashboard, monitoring, hardening, full privacy review	US-15, US-17, US-18, PRIV-02, TECH-04	MVP ready for the pilot
6	Feb 1 to Feb 12	Store	Pilot, bug fixing, handover. No new stories	None	Real shoppers use it. Final presentation

2. Estimates of macro items

Relative sizes: S is about 1.5 person-days, M about 4, L about 8. Stories marked Later (US-16, compare two sizes) are not included. Privacy and Platform are new epics for the work added at the 3a and 3b reviews (D15, D22): 24.5 person-days in all, less 4 for US-16 moved to Later.

Epic	Stories	Person-days
Start	US-01, US-02, US-03	7
Avatar	SP-01, US-04, US-05, US-06, US-11	21.5
Browse	US-07	4
Try on	SP-02, US-08	9.5
Fit	US-09, US-10	12
Buy	US-12	4
Store	US-13, US-14, US-23, US-17	16
After purchase	US-15	1.5
Dashboard	US-18	8
Operations and data	OPS-01, US-22, OPS-02	9.5
Privacy	PRIV-01, PRIV-02	5.5
Platform	TECH-01, TECH-02, TECH-03, TECH-04	13.5
Total		**112**

Capacity check

Item	Person-days
Capacity assumed: 4 people, about 3 days a week each, 6 days each per sprint, 24 per sprint, sprints 1 to 5	120
Work planned in sprints 1 to 5	112
Slack	8 (7%)

The capacity assumption must be confirmed by each member. Planned load by sprint:

Sprint	Planned person-days	Capacity	Load
1	23.5	24	98%
2	21.5	24	90%
3	24	24	100%
4	24	24	100%
5	19	24	79%

Sprints 1, 3 and 4 are full or nearly full, and total slack is only 8 person-days (7%). If sprint 1 slips, TECH-03 and SP-02 move first, because the avatar spike and the data request come before them. If sprint 3 slips, US-10 or US-09 loses the safety margin first. That is why US-11 (a Should) sits in sprint 4, not sprint 3. Sprint 5 has 5 days of room, which is where US-16 can return if the velocity check allows (R18). Sprint 6 has no new stories, so it absorbs slips.

3. Obstacles to watch

Obstacle	Link	What we do
Kiabi data or access arrives late	R2, R13, R15	Send the data request in week 1 (OPS-01), with garment images, a card-number check and the privacy contact. Fallback: 20 hand-prepared articles
The avatar looks wrong on real photos	R7	The spike and sprint 2 exist to find this out early

Obstacle	Link	What we do
Holidays and exams cut sprint 4 capacity	R11	Re-plan at the start of sprint 4
No pilot shop confirmed	R14	Ask Kiabi in sprint 1. Fallback: staff-only demo
Privacy question blocks the pilot	R9	Privacy checklist in sprint 1 (PRIV-01), before any photo from outside the team. Full privacy review in sprint 5 (PRIV-02) before real shoppers (D10, D22)
Technical work takes the capacity planned for stories	R18, R19	Check velocity in sprints 1 and 2. If it is under 20 person-days, keep US-16 in Later and name a back-end backup (D15)
The pilot shop network is too weak for the mirror and the tablet	R17	Signal test before sprint 4 (OPS-02), polling fallback (D20). Last fallback: staff-only demo

4. How the pilot is measured

Rule	Detail
Control group	Shoppers who see the same articles without try-on, same weeks
Main metric	Return rate on pilot articles against the 26.5% baseline
Second metric	Fitting grade among users who tried on, against the 3 out of 10 baseline
Reported	At each sprint review, by Hadeed

5. Gandalf checkpoint calendar

The Gandalf deadline for every checkpoint is 2026-11-06. All checkpoint documents were essentially complete on 2026-11-04, two days ahead of the deadline. The brief itself does not publish checkpoint dates.

Checkpoint	File	Gandalf deadline
1a	submission/1a_product-manifesto.pdf	2026-11-06
1b	submission/1b_team-and-rituals.pdf	2026-11-06
2a	submission/2a_personas.pdf	2026-11-06
2b	submission/2b_storymap.pdf	2026-11-06
3a	submission/3a_target-architecture.pdf	2026-11-06
3b	submission/3b_risk-management.pdf	2026-11-06
A	submission/A_roadmap.pdf	2026-11-06
B	submission/B_methodology.pdf	2026-11-06
C	submission/C_backlog-and-decision-log.pdf	2026-11-06
