Final deliverable B. Project methodology and rituals

Project: Fittybird x Kiabi, 360° Framework
Deliverable: B, Period 4 (implementation process)
Terms: `shared/glossary.docx`


1. Method chosen: Scrum with a Kanban board

The team works in two-week Scrum sprints and manages the flow on a Kanban board with a limit on work in progress.

Why Scrum	Why a Kanban board
Fixed review and retro dates match what Kiabi and the school expect	A limit on work in progress stops four people from starting everything at once
A sprint goal keeps the team on the riskiest items first	A visible flow shows blockers early

Alternatives considered: pure Kanban (no fixed review dates, so Kiabi gets no regular demo) and pure Scrum (no work-in-progress limit, which risks half-finished stories). Logged as decision D13.

2. The sprint loop and its rituals

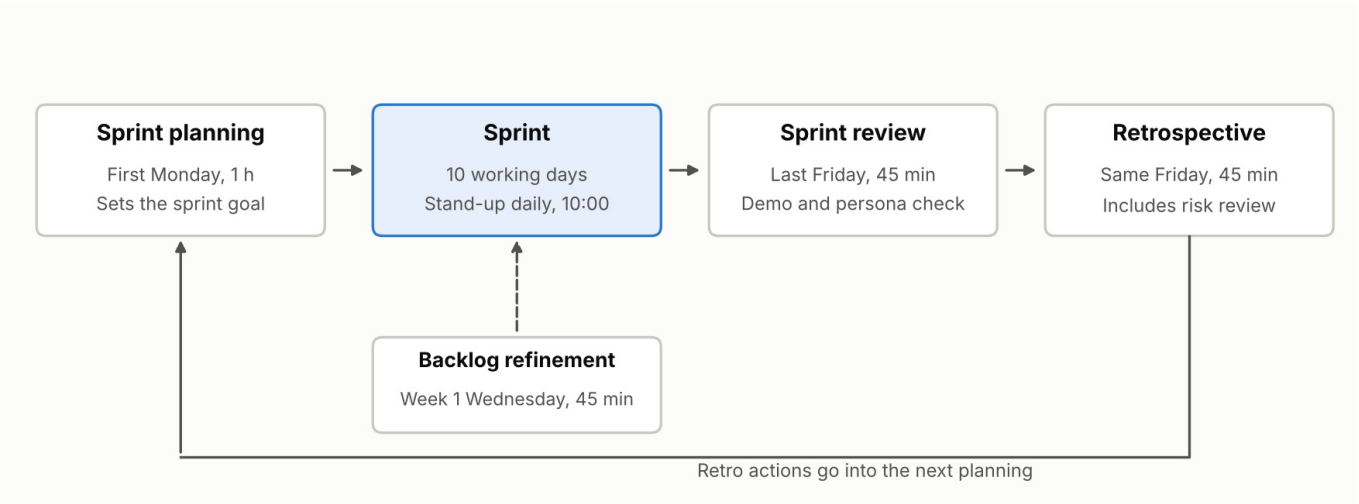

Ritual	When	Length	Who	Output
Sprint planning	First Monday of a sprint	1 hour	Whole team	Sprint goal and stories. Each story names a persona
Daily stand-up	Every working day, 10:00	15 minutes	Whole team	Yesterday, today, blockers
Backlog refinement	Wednesday of week 1	45 minutes	Whole team	Stories that meet the Definition of Ready
Sprint review	Last Friday	45 minutes	Team and Kiabi sponsor when available	Demo through one persona's journey, KPI report, feedback
Retrospective	Same Friday, after the review	45 minutes	Whole team	Up to 3 actions with owners
Risk review	Inside the retro	15 minutes	Whole team	Risks re-scored by the team (`3b-risks/risk-management.docx`)
Checkpoint review	Before each Gandalf hand-in	30 minutes	Whole team	Decisions written in `C-backlog/decision-log.docx`

3. First version of the board

Column	Holds	Rule
Backlog	All stories, ordered by priority and risk	Only the product manager reorders
Ready	Stories that meet the Definition of Ready	Pulled in at sprint planning

In progress	Stories being built	At most 4 at a time
In review	Built stories waiting for a second pair of eyes	Review within one working day
Done	Stories that meet the Definition of Done	Shown at the sprint review

A blocked story gets a Blocked tag and is raised at the next stand-up. Sprint 1 starts with SP-01, US-01, US-02, US-03 and OPS-01 in Ready. The board tool is chosen in sprint 1, with the repository host in mind.

4. Definitions

Definition	Conditions
Ready	The story names a persona and the Kiabi data behind it. It has acceptance criteria, a size and no unanswered dependency
Done	Acceptance criteria pass. A second person reviewed the work. It runs in staging. The product manager has seen it in a sprint review. Events needed for its KPI are tracked

5. Indicators to monitor

Targets are proposals. The team adjusts them after sprint 2.

Indicator	What it tells	Target	Reported by
Sprint goal reached	Whether planning is realistic	5 of 6 sprints	Elie
Velocity	Person-days of Done stories per sprint	About 16 to 24, the pace the backlog needs	Elie
Open red risks	Whether risks are being retired	Falls every sprint	Elie
Avatar success rate	Share of test photo sets that give a usable avatar	80% by the end of sprint 2	Muhammad
Size match	Share of testers whose advised size is their real size	80% from sprint 3	Hadeed
Stories with a persona	Whether the user's point of view is kept	100%	Boyu
Return rate on pilot articles	The business effect, against the 26.5% baseline	Fall of 3 points against the control group	Hadeed

6. How the method keeps the user in view

- Each story names one persona, so a developer always knows who the work is for (`2a-personas/personas.docx`).
- Each sprint review replays one persona's journey end to end.
- Each retro includes a risk review, so risks are not scored by one person.
- Each checkpoint review updates the decision log, so choices stay traceable.
